

POSTAL TELEGRAPH - COMMERCIAL CABLES

CLARENCE H. MACKAY, PRESIDENT.

RECEIVED AT

TELEGRAM

DELIVERY NO.

This is a fast Telegram unless otherwise indicated by signal after the number of words:—"Blue" (Day Letter) "N.L." (Night Letter) or "Nite" (Night Telegram) Form 16

STANDARD TIME INDICATED ON THIS MESSAGE.

R139GSSD 714P 51 BLUE

925 NOV 14 '22

NEWYORK NY NOV 14 22

MISS JULIA MORGAN

ARCHITECT MER EXCHANGE BLG SANFRANCISCO

SUGGEST DISCHARGING CONSTRUCTION FORCE ENTIRELY DURING WINTER MEN CANNOT
WORK MATERIAL CANNOT BE TRANSPORTED STORMS UNDO WORK DONE EXPENSE
LARGE AND USELESS HOW LONG WOULD IT TAKE TO CARRY WALLS TO FIRST FLOOR
AND FLOOR THAT IS OVERHEAD WOULD LIKE TO STOP DECEMBER FIRST AND
BEGIN AGAIN MARCH FIRST PLEASE ADVISE

HEARST

Amo - Nov 15th

Rossi begin
pouring concrete
in four ft
1st floor to heavy
tube about 2 ft
if weather good
may not slip
down at top
but strong walls
perhaps by end
of year - surely

RECEIVED 11/15/32



RECEIVED 11/15/32

MISSING 11/15/32

ARCHITECT EXCHANGE BLDG SAN FRANCISCO

BEGIN AGAIN MARCH FIRST PLEASE ADVISE
AND FLOOR THAT IS OVERHEAD WOULD LIKE TO STOP DECEMBER FIRST AND
LARGE AND USELESS HOW LONG WOULD IT TAKE TO CARRY WALLS TO FIRST FLOOR
WORK MATERIAL CANNOT BE TRANSPORTED STORMS UNDO WORK DONE EXPENSE
SUGGEST DISCHARGING CONSTRUCTION FORCE ENTIRELY DURING WINTER MEN CANNOT

RECEIVED

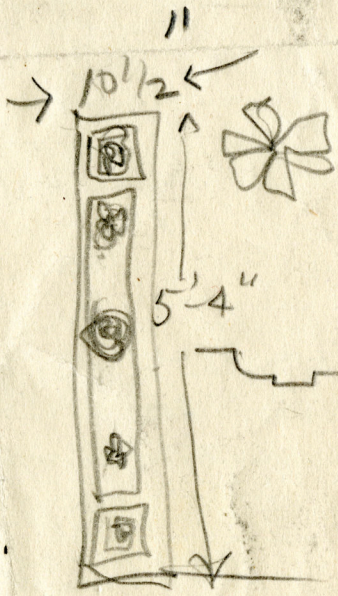

COMMERCIAL CABLES

GRAM

DELIVERY NO.

RECEIVED 11/15/32
